TWO WEEK LOOK AHEAD SCHEDULE

PROJECT: DCKA-2021-C-0025 Cleveland Park Streetscape & Drainage Improvements

CAPITOL PAVING OF D.C., INC

Week Start:	Tue, 4/25/2023
Today Date:	Tue, 4/25/2023
Display Week:	1
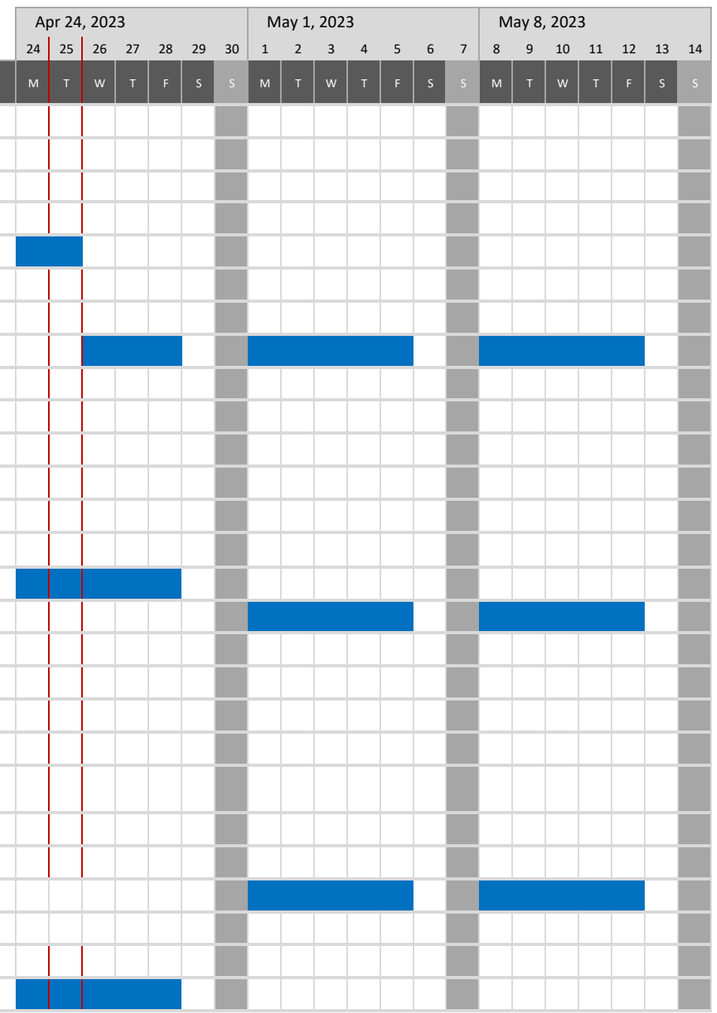
ID	ACTIVITY	RESOURCE	COMMENTS	PROGRESS	START	END	DURATION
DCKA-2021-C-0025.6	**Pre-Construction**				**3/10/22**	**3/25/22**	**411**
A1540	Project Stake Out & Lay Out	CPDC		85%	3/7/22		
DCKA-2021-C-0025.7.1	**Phase 1 (ORDWAY ST)**				**3/21/22**		**400**
A11190	PH1H Install Stormdrain MH 3-7, MH 3-8, MH 10-1, MH 10-2, I 3-7, I 10-3	CPDC	Basins Remaining	85%	3/6/23	4/25/23	50.00
A11210	PH1I Install Stormdrain I3-6, I10-1, I10-2, & RCP	CPDC	Pending on PEPCO pole bracing	0%			0.00
A11170	PH1D-H Relocate Watermain	CPDC		60%	2/15/23	3/16/23	29.00
A11175-CO	CO: Additional Watermain @ Conn. & Ordway	CPDC		0%	4/26/23	5/13/23	17.00
A11220	PH1 Perform CCTV Inspection	CPDC		50%	12/1/22	12/2/22	1.00
A11250	PH1 Restore Utility PCC Base	CPDC		40%	2/7/23	2/18/23	11.00
DCKA-2021-C-0025.7.2	**Phase 2 (SERVICE LANE)**				**2/27/2023**		**57**
A2040	PH2 Install PCC Curb/Gutter, PCC Sidewalk Base, ADA WCR Sta. 1002+25 to Sta. 1010+00	CPDC		90%	3/1/23	4/14/23	44.00
A2090	PH2 Install Cobblestone Pavers, Thermal Stone Pavers, Cabblestone Pavers, Concrete Block Pa	RCE		90%	3/20/23	4/15/23	26.00
A2015	PH2 PEPCO Reset Manhole and Vaults	PEPCO	Waiting for grates	75%	3/9/23	4/10/23	32.00
A2090	PH2B Demo Existing Sidewalk & Install Proposed block Sidewalk Sta. 2000+00 to 2004+00	CPDC/RCE		40%	4/17/23	4/29/23	12.00
A2100	PH2B Demo Existing Sidewalk & Install Proposed block Sidewalk Sta. 2004+00 to 2008+00	CPDC/RCE		0%	4/30/23	5/15/23	15.00
A2080	PH2 Install Porous Rubber Sidewalk	CapitplFelx		0%			0.00
DCKA-2021-C-0025.7.3	**Phase 3 (PORTER ST)**				**3/21/2022**		**400**
A3260	PH3A Install PCC Sidewalk, Stone Paver Thermal, Cobblestone edging, Masonry Stone and Plan	RCE	coping masonry to complete	95%	3/15/23	3/17/23	2.00
DCKA-2021-C-0025.7.4	**Phase 4 (SB CT Ave)**				**11/28/2022**		**148**
A4025	PH4 Install New Curb/Gutter Layout, Sidewalk & ADA WCR @ Inter Newark St & Conn. Ave	CPDC/RCE	pending Consigli demobilization of construction fence	0%			0.00
DCKA-2021-C-0025.7.6.2	**Permanent Traffic & Streeligting**				**10/31/2022**		**176**
	Install Traffic & Streetlight Poles, Fixtures, & Cable at Porter St & Quebec St Inter	MC DEAN	completed	100%	3/20/23	4/14/23	25.00
A1575	Install Electrical Conduit at Ordway St & Conn. Ave Inter	MC DEAN		90%	11/2/22	5/13/23	192.00
A1560	Install Elctrical Manholes & Conduit at Macomb St & Conn. Ave Inter	MC DEAN		95%	2/27/23	4/8/23	40.00
	Install Traffic Pole & Fixtures & Cable at Ordway & Conn. Ave Inter	MC DEAN		90%	4/17/23	4/22/23	5.00
	Install Traffic Pole & Fixtures & Cable at Macomb & Conn. Ave Inter	MC DEAN		20%	4/17/23	5/6/23	19.00
