TWO WEEK LOOK AHEAD SCHEDULE

PROJECT: DCKA-2021-C-0025 Cleveland Park Streetscape & Drainage Improvements

CAPITOL PAVING OF D.C., INC

Week Start: Tue, 4/11/2023
Today Date: Tue, 4/11/2023
Display Week: 1
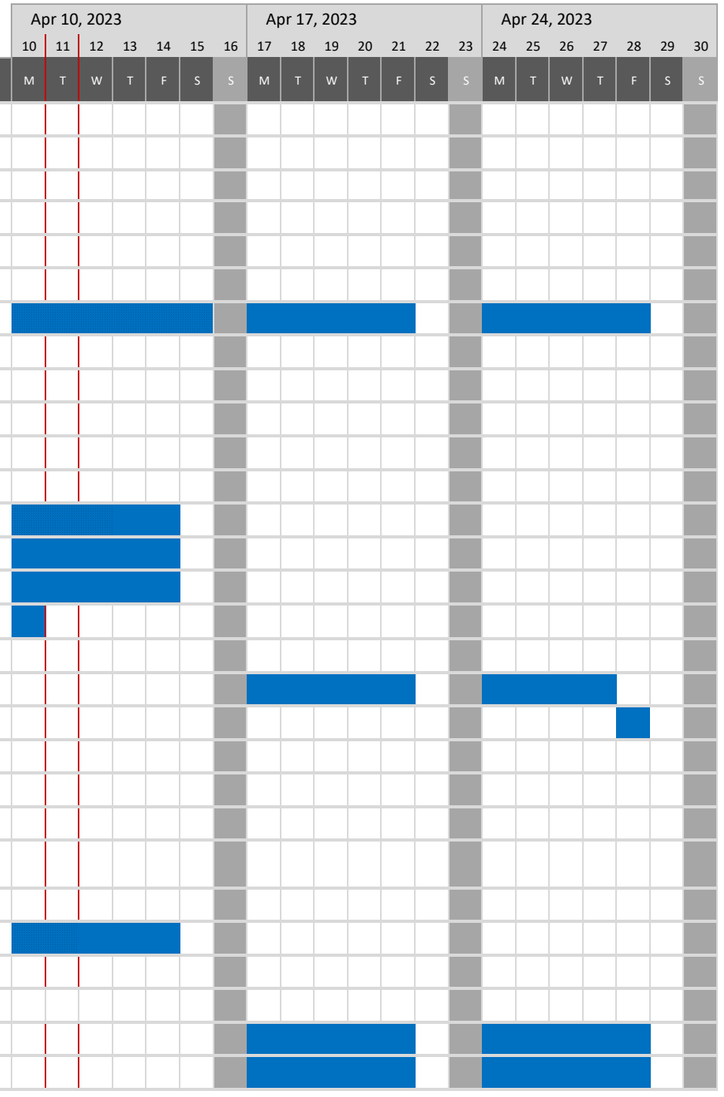
ID	ACTIVITY	RESOURCE	COMMENTS	PROGRESS	START	END	DURATION
DCKA-2021-C-0025.6 Pre-Construction					**3/10/22**	**3/25/22**	**397**
A1540	Project Stake Out & Lay Out	CPDC		85%	3/7/22		
DCKA-2021-C-0025.7.1 Phase 1 (ORDWAY ST)					**3/21/22**		**386**
A11180	PH1F-G Install Stormdrain RCP	CPDC	Dependent on watermainwork	30%	1/13/23	3/15/23	61.00
A11190	PH1H Install Stormdrain MH 3-7, MH 3-8, MH 10-1, MH 10-2, I 3-7, I 10-3	CPDC	MH 3-7	30%	3/6/23	4/7/23	32.00
A11200	PH1H Install RCP	CPDC		60%	3/13/23	10/14/23	215.00
A11250	PH1 Restore Utility PCC Base	CPDC		40%	2/7/23	2/18/23	11.00
A11170	PH1D-H Relocate Watermain	CPDC		30%	2/15/23	3/16/23	29.00
	Watermain Shutdown (NIGHT WORK)	CPDC	completed	100%	3/16/23	3/16/23	0.00
A11220	PH1 Perform CCTV Inspection	CPDC		50%	12/1/22	12/2/22	1.00
DCKA-2021-C-0025.7.2 Phase 2 (SERVICE LANE)					**2/27/2023**		**43**
A2030	PH2 Demo Existing Travel Lane, Reset MH/Vault Covers, 4" PVC Connect Pipe, Prop. PCC Trave	CPDC		90%	3/26/23	4/14/23	19.00
A2040	PH2 Install PCC Curb/Gutter, PCC Sidewalk Base, ADA WCR Sta. 1002+25 to Sta. 1010+00	CPDC		80%	3/1/23	4/14/23	44.00
A2090	PH2 Install Cobblestone Pavers, Thermal Stone Pavers, Cabblestone Pavers, Concrete Block Pa	RCE		80%	3/20/23	4/15/23	26.00
A2015	PH2 PEPCO Reset Manhole and Vaults	PEPCO	Waiting for grates	75%	3/9/23	4/10/23	32.00
A2080	PH2 Install Porous Rubber Sidewalk	CapitplFelx	pending submittal approval	0%	4/10/23		-45026.00
A2090	PH2B Demo Existing Sidewalk & Install Proposed block Sidewalk Sta. 2000+00 to 2004+00	CPDC/RCE		0%	4/17/23	4/27/23	10.00
A2100	PH2B Demo Existing Sidewalk & Install Proposed block Sidewalk Sta. 2004+00 to 2008+00	CPDC/RCE		0%	4/28/23	5/13/23	15.00
DCKA-2021-C-0025.7.3 Phase 3 (PORTER ST)					**3/21/2022**		**386**
A3260	PH3A Install PCC Sidewalk, Stone Paver Thermal, Cobblestone edging, Masonry Stone and Plar	RCE	coping masonry to complete	95%	3/15/23	3/17/23	2.00
DCKA-2021-C-0025.7.4 Phase 4 (SB CT Ave)					**11/28/2022**		**134**
A4025	PH4 Install New Curb/Gutter Layout, Sidewalk & ADA WCR @ Inter Newark St & Conn. Ave	CPDC/RCE	pending Consigli demobilization of construction fence	0%			0.00
DCKA-2021-C-0025.7.6.2 Permanent Traffic & Streeligting					**10/31/2022**		**162**
	Install Traffic & Streetlight Poles, Fixtures, & Cable at Porter St & Quebec St Inter	MC DEAN		90%	3/20/23	4/14/23	25.00
A1575	Install Electrical Conduit at Ordway St & Conn. Ave Inter	MC DEAN		90%	11/2/22	4/8/23	157.00
A1560	Install Elctrical Manholes & Conduit at Macomb St & Conn. Ave Inter	MC DEAN		95%	2/27/23	4/8/23	40.00
	Install Traffic Pole & Fixtures & Cable at Macomb & Conn. Ave Inter	MC DEAN		0%	4/17/23	5/2/23	15.00
	Install Traffic Pole & Fixtures & Cable at Ordway & Conn. Ave Inter	MC DEAN		0%	4/17/23	5/2/23	15.00
