# TWO WEEK LOOK AHEAD SCHEDULE

## PROJECT: DCKA-2021-C-0025 Cleveland Park Streetscape & Drainage Improvements

CAPITOL PAVING OF D.C., INC

| | |
|---|---|
| Week Start: | Tue, 5/23/2023 |
| Today Date: | Tue, 5/23/2023 |
| Display Week: | 1 |
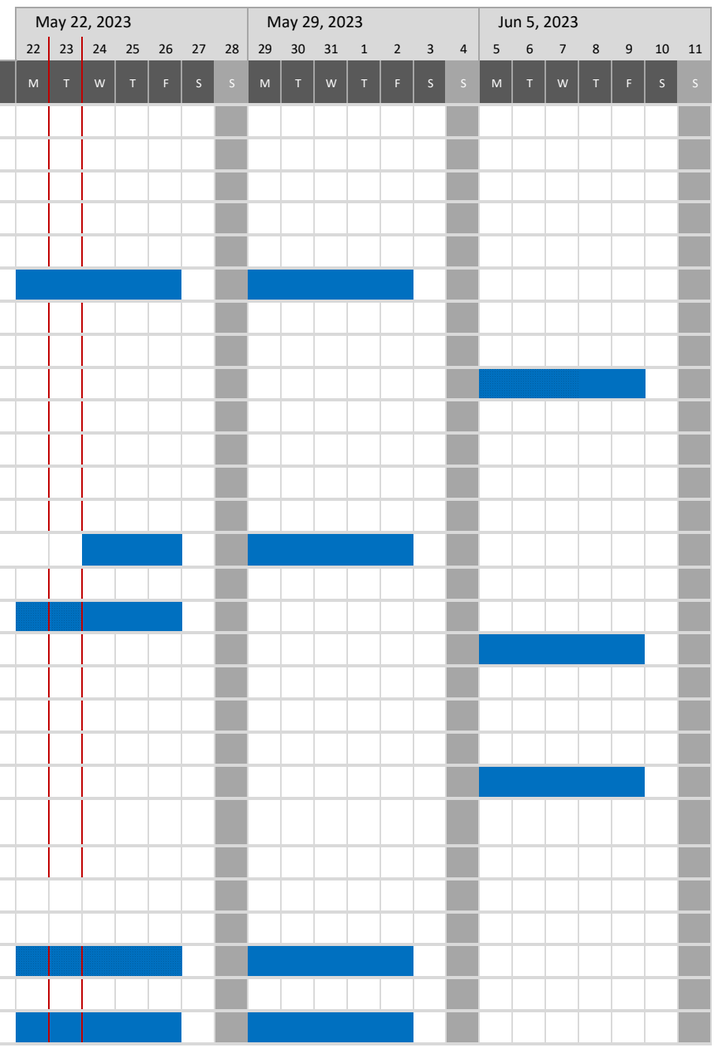
| ID | ACTIVITY | RESOURCE | COMMENTS | PROGRESS | START | END | DURATION |
|---|---|---|---|---|---|---|---|
| **DCKA-2021-C-0025.6** | **Pre-Construction** | | | | **3/10/22** | **3/25/22** | **439** |
| A1540 | Project Stake Out & Lay Out | CPDC | | 85% | 3/7/22 | | |
| **DCKA-2021-C-0025.7.1** | **Phase 1 (ORDWAY ST)** | | | | **3/21/22** | | **428** |
| A11190 | PH1H Install Stormdrain MH 3-7, MH 3-8, MH 10-1, MH 10-2, I 3-7, I 10-3 | CPDC | Basins Remaining | 85% | 3/6/23 | 4/25/23 | 50.00 |
| A11210 | PH1I Install Stormdrain I3-6, I10-1, I10-2, & RCP | CPDC | | 50% | 5/15/23 | 6/2/23 | 18.00 |
| A11170 | PH1D-H Relocate Watermain | CPDC | completed | 100% | 2/15/23 | 3/16/23 | 29.00 |
| A11175-CO | CO: Additional Watermain @ Conn. & Ordway | CPDC | completed | 100% | 4/26/23 | 5/13/23 | 17.00 |
| A11220 | PH1 Perform CCTV Inspection | CPDC | | 50% | 6/5/23 | 6/10/23 | 5.00 |
| A11250 | PH1 Restore Utility PCC Base | CPDC | | 40% | 2/7/23 | 2/18/23 | 11.00 |
| **DCKA-2021-C-0025.7.2** | **Phase 2 (SERVICE LANE)** | | | | **2/27/2023** | | **85** |
| A2040 | PH2 Install PCC Curb/Gutter, PCC Sidewalk Base, ADA WCR Sta. 1002+25 to Sta. 1010+00 | CPDC | | 90% | 3/1/23 | 4/14/23 | 44.00 |
| A2090 | PH2 Install Cobblestone Pavers, Thermal Stone Pavers, Cabblestone Pavers, Concrete Block Pa | RCE | | 90% | 3/20/23 | 4/15/23 | 26.00 |
| A2015 | PH2 PEPCO Reset Manhole and Vaults | PEPCO | | 75% | 3/9/23 | 6/2/23 | 85.00 |
| A2090 | PH2B Demo Existing Sidewalk & Install Proposed block Sidewalk Sta. 2000+00 to 2004+00 | CPDC/RCE | | 95% | 4/17/23 | 5/5/23 | 18.00 |
| A2100 | PH2B Demo Existing Sidewalk & Install Proposed block Sidewalk Sta. 2004+00 to 2008+00 | CPDC/RCE | | 80% | 5/6/23 | 5/28/23 | 22.00 |
| A2080 | PH2 Install Porous Rubber Sidewalk | CapitplFelx | | 0% | 6/5/23 | 6/15/23 | 10.00 |
| **DCKA-2021-C-0025.7.3** | **Phase 3 (PORTER ST)** | | | | **3/21/2022** | | **428** |
| A3260 | PH3A Install PCC Sidewalk, Stone Paver Thermal, Cobblestone edging, Masonry Stone and Plan | RCE | coping masonry to complete | 95% | 3/15/23 | 3/17/23 | 2.00 |
| **DCKA-2021-C-0025.7.4** | **Phase 4 (SB CT Ave)** | | | | **11/28/2022** | | **176** |
| A4025 | PH4 Install New Curb/Gutter Layout, Sidewalk & ADA WCR @ Inter Newark St & Conn. Ave | CPDC/RCE | | 0% | 6/5/23 | 6/15/23 | 10.00 |
| A4025 | PH4 Install Sidewalk | CPDC/RCE | pending Consigli demobilization of construction fence | 0% | | | 0.00 |
| **DCKA-2021-C-0025.7.6.2** | **Permanent Traffic & Streeligting** | | | | **10/31/2022** | | **204** |
| A1575 | Install Electrical Conduit at Ordway St & Conn. Ave Inter | MC DEAN | | 90% | 11/2/22 | 5/13/23 | 192.00 |
| A1560 | Install Elctrical Manholes & Conduit at Macomb St & Conn. Ave Inter | MC DEAN | Pending RFI 78 | 95% | 2/27/23 | 4/8/23 | 40.00 |
| | Install Traffic Pole & Fixtures & Cable at Ordway & Conn. Ave Inter | MC DEAN | | 90% | 4/17/23 | 6/2/23 | 46.00 |
| | Install Traffic Pole & Fixtures & Cable at Macomb & Conn. Ave Inter | MC DEAN | | 20% | 4/17/23 | 5/19/23 | 32.00 |
| | Install Communication Cable | MC DEAN | | | 5/22/23 | 6/3/23 | 12.00 |
