TWO WEEK LOOK AHEAD SCHEDULE

PROJECT: DCKA-2021-C-0025 Cleveland Park Streetscape & Drainage Improvements

CAPITOL PAVING OF D.C., INC

Week Start: Tue, 3/14/2023
Today Date: Tue, 3/14/2023
Display Week: 1
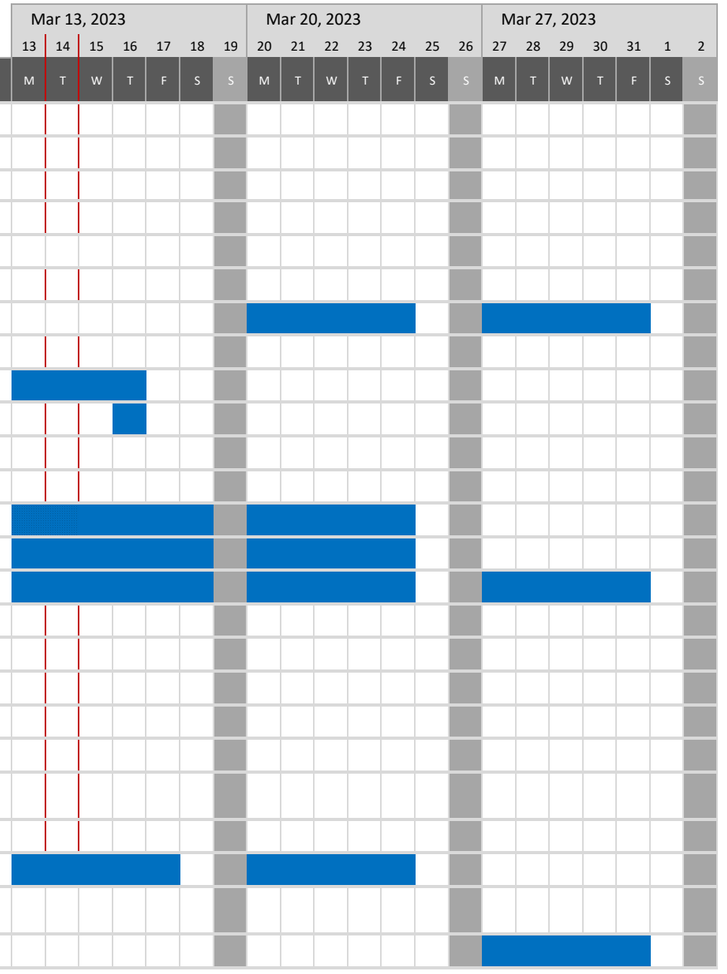
ID	ACTIVITY	RESOURCE	COMMENTS	PROGRESS	START	END	DURATION
DCKA-2021-C-0025.6 Pre-Construction					**3/10/22**	**3/25/22**	**369**
A1540	Project Stake Out & Lay Out	CPDC		85%	3/7/22		
DCKA-2021-C-0025.7.1 Phase 1 (ORDWAY ST)					**3/21/22**		**358**
A11180	PH1F-G Install Stormdrain RCP	CPDC	Dependent on watermainwork	30%	1/13/23	3/15/23	61.00
A11190	PH1H Install Stormdrain MH 3-7, MH 3-8, MH 10-1, MH 10-2, I 3-7, I 10-3	CPDC	MH 3-7	0%	3/6/23	3/11/23	5.00
A11200	PH1H Install RCP	CPDC		0%	3/13/23	4/2/23	20.00
A11250	PH1 Restore Utility PCC Base	CPDC		40%	2/7/23	2/18/23	11.00
A11170	PH1D-H Relocate Watermain	CPDC		20%	2/15/23	3/16/23	29.00
	Watermain Shutdown (NIGHT WORK)	CPDC	tentaive - waiting on DC confirmation	0%	3/16/23	3/16/23	0.00
A11220	PH1 Perform CCTV Inspection	CPDC		50%	12/1/22	12/2/22	1.00
DCKA-2021-C-0025.7.2 Phase 2 (SERVICE LANE)					**2/27/2023**		**15**
A2020	PH2 Demo Existing Travel Lane, Reset MH/Vault Covers, 4" PVC Connect Pipe, Prop. PCC Trave	CPDC		55%	3/1/23	3/26/23	25.00
A2040	PH2 Install PCC Curb/Gutter, PCC Sidewalk Base, ADA WCR Sta. 1002+25 to Sta. 1010+00	CPDC		30%	3/1/23	3/26/23	25.00
A2015	PH2 PEPCO Reset Manhole and Vaults	PEPCO		10%	3/9/23	4/20/23	42.00
DCKA-2021-C-0025.7.3 Phase 3 (PORTER ST)					**3/21/2022**		**358**
A3190	PH3A Install PCC Coping, Art Foundation, PCC Curb/Gutter, ADA WCR, PCC Base	CPDC		90%	10/7/22	3/10/23	154.00
	PH3A PEPCO Reset Manhole	PEPCO		50%	3/1/23	3/10/23	9.00
	Coping Wall Masonry Stone	RCE		95%	1/3/23	1/11/23	8.00
DCKA-2021-C-0025.7.4 Phase 4 (SB CT Ave)					**11/28/2022**		**106**
A4025	PH4 Install New Curb/Gutter Layout, Sidewalk & ADA WCR @ Inter Newark St & Conn. Ave	CPDC/RCE	pending Consigli demobilization of construction fence	0%			0.00
DCKA-2021-C-0025.7.6.2 Permanent Traffic & Streeligting					**10/31/2022**		**134**
A1590	Install Electrical Manholes & Conduit at Quebec & Porter St Inter	MC DEAN		70%	10/31/22	3/24/23	144.00
A1575	Install Electrical Conduit at Ordway St & Conn. Ave Inter	MC DEAN	pending on PEPCO Cons team to make conduit connection	70%	11/2/22	2/24/23	114.00
A1560	Install Elctrical Manholes & Conduit at Macomb St & Conn. Ave Inter	MC DEAN		30%	2/27/23	3/31/23	32.00
