TWO WEEK LOOK AHEAD SCHEDULE

PROJECT: DCKA-2021-C-0025 Cleveland Park Streetscape & Drainage Improvements

CAPITOL PAVING OF D.C., INC

Week Start:	Mon, 8/14/2023
Today Date:	Tue, 8/15/2023
Display Week:	1
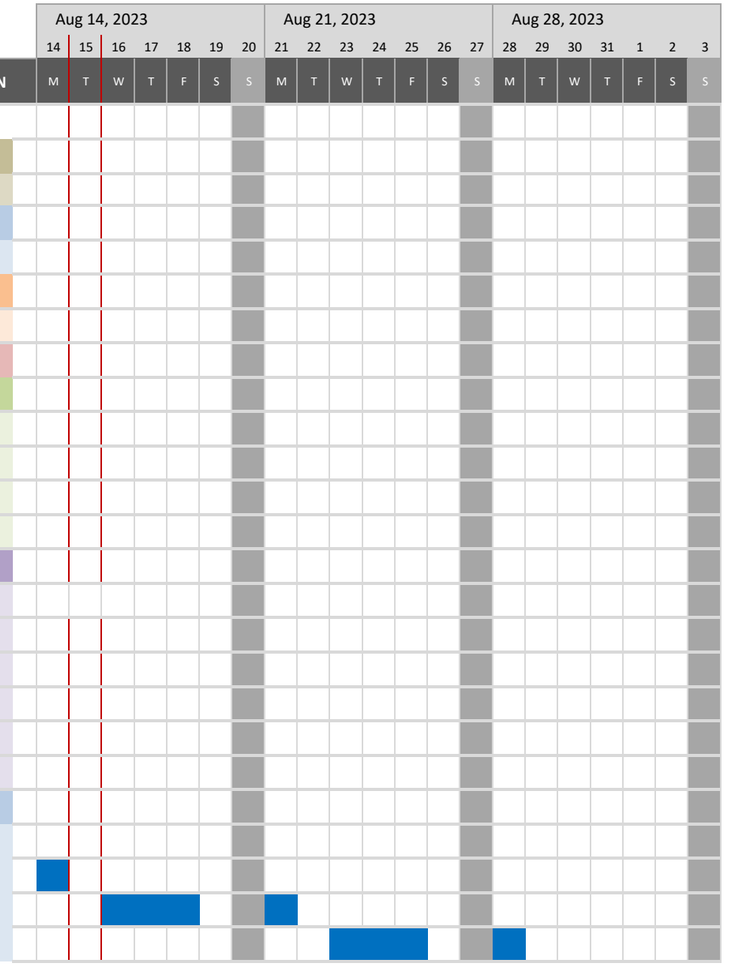
ID	ACTIVITY	RESOURCE	COMMENTS	PROGRESS	START	END	DURATION
DCKA-2021-C-0025.6	**Pre-Construction**				**3/10/22**	**3/25/22**	**523**
A1540	Project Stake Out & Lay Out	CPDC		85%	3/7/22		
DCKA-2021-C-0025.7.1	**Phase 1 (ORDWAY ST)**				**3/21/22**		**512**
A11220	PH1 Perform CCTV Inspection	INISGHT		50%	7/18/23	7/18/23	0.00
DCKA-2021-C-0025.7.2	**Phase 2 (SERVICE LANE)**				**2/27/2023**		**169**
A2080	PH2 Install Porous Rubber Sidewalk	CapitplFelx	onhold	0%			0.00
DCKA-2021-C-0025.7.3	**Phase 3 (PORTER ST) - COMPLETED**				**3/21/2022**		**512**
DCKA-2021-C-0025.7.4	**Phase 4 (SB CT Ave)**				**11/28/2022**		**260**
A4025	PH4 Install Sidewalk & Misc Items	CPDC/RCE	on hold - pending DDOT Final Decsion	0%			0.00
	Install FD Driveway	CPDC	Completed	100%	7/5/23	7/17/23	12.00
	Install WCR @ Macomb St Inter	CPDC		0%	7/26/23	7/29/23	3.00
	Restore Misc UT PCC Base	CPDC		0%	7/17/23	7/23/23	6.00
DCKA-2021-C-0025.7.6.2	**Permanent Traffic & Streeligting**				**10/31/2022**		**288**
A1560	Install Elctrical Manholes & Conduit at Macomb St & Conn. Ave Inter	MC DEAN		95%	2/27/23	6/10/23	103.00
	Install Traffic Pole & Fixtures & Cable at Macomb & Conn. Ave Inter	MC DEAN		70%	6/5/23	6/16/23	11.00
	Install Communication Cable	MC DEAN	Bloackages	100%	5/22/23	7/29/23	68.00
	Push Buttons at fire house	MC DEAN	Waiting on DDOT	0%			
	Removal of temp items	MC DEAN	Waiting on DDOT	0%			
	Conduit Bloackages	MC DEAN		100%	6/12/23	7/22/23	40.00
DCKA-2021-C-0025.7.5	**Phase 5 (M&P)**				**3/21/22**		**512**
A5000	Asphalt Milling Connecticut Ave & Side Streets	METRO	NIGHTWORK	100%	7/31/23	8/5/23	5.00
A5010	Asphalt Paving Connectut Ave & Side Streets	METRO	NIGHTWORK	90%	8/7/23	8/14/23	7.00
A5030	Installation of Pavement Marking	Equus		0%	8/16/23	8/21/23	5.00
A5030	Installation of Pavement Signage	CPDC		0%	8/23/23	8/28/23	5.00
