TWO WEEK LOOK AHEAD SCHEDULE

PROJECT: DCKA-2021-C-0025 Cleveland Park Streetscape & Drainage Improvements

CAPITOL PAVING OF D.C., INC

Week Start:	Tue, 10/24/2023
Today Date:	Tue, 10/24/2023
Display Week:	1
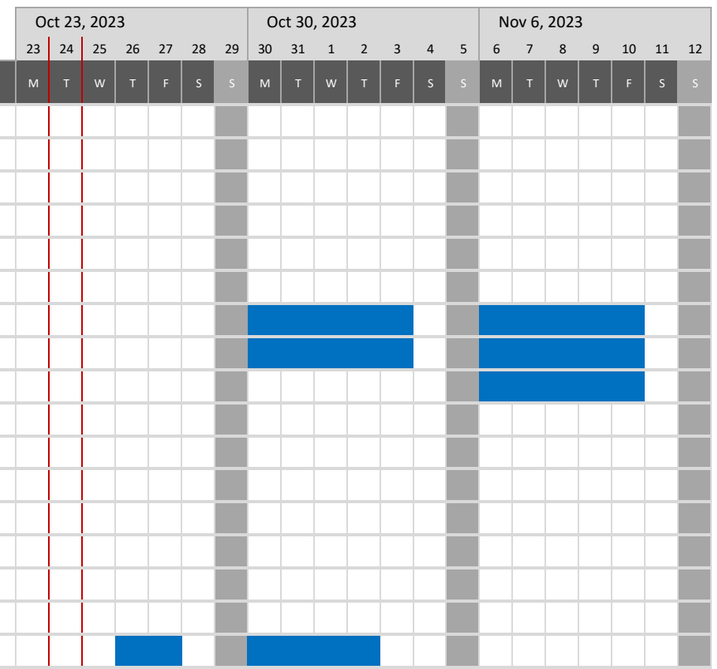
ID	ACTIVITY	RESOURCE	COMMENTS	PROGRESS	START	END	DURATION
DCKA-2021-C-0025.6	**Pre-Construction - COMPLETED**				**3/10/22**	**3/25/22**	**15**
DCKA-2021-C-0025.7.1	**Phase 1 (ORDWAY ST)**				**3/21/22**	**7/25/23**	**491**
	Final DC Water Inspection Walkthrough	Various	Completed	100%	10/3/23	10/3/23	0.00
DCKA-2021-C-0025.7.2	**Phase 2 (SERVICE LANE)**				**2/27/2023**	**8/7/23**	**161**
DCKA-2021-C-0025.7.2.1	**Service Lane Modification**				**10/30/2023**		**-6**
CO-A11270	Order & Precure Add Material (CO)	Cold Spring	1st Delivery week 10/30, 2nd 10/6	0%	10/30/23	11/11/23	12.00
CO-A11285	Remove Existing Pavers	CPDC	Tentative	0%	10/30/23	11/14/23	15.00
CO-A11280	Replace Pavers (CO)	RCE		0%	11/6/23	11/26/23	20.00
DCKA-2021-C-0025.7.3	**Phase 3 (PORTER ST) - COMPLETED**				**3/21/2022**	**6/17/23**	**453**
DCKA-2021-C-0025.7.4	**Phase 4 (SB CT Ave) - COMPLETED**				**11/28/2022**	**8/22/23**	**267**
DCKA-2021-C-0025.7.6.2	**Permanent Traffic & Streeligting**				**10/31/2022**		**358**
	Bump & Activate Instesction @ Orway St	MC DEAN	Pending on DDOT	0%			0.00
DCKA-2021-C-0025.7.5	**Phase 5 (M&P) - COMPLETED**				**8/1/2023**	**8/16/23**	**15**
DCKA-2021-C-0025.7.7	**Landscaping**				**10/17/2023**		**7**
	Install Planting Soil in Tree Space	CPDC	Completed	100%	10/18/23	10/21/23	3.00
A1960	Installation of Topsoil, Mulch, Shurbs/Parennials & Trees	E&F		0%	10/26/23	11/2/23	7.00
